

FY 2022-23 4th Quarter Project Delivery Report


by Jeffrey N. Wiley


Project Delivery Performance Measures

Measure	FY 2022-23 Planned	FY 2022-23 Completed	% Completed	Last Five Fiscal Year Average
Draft Environmental Documents	70	53	76%	81%
Project Approval, Environmental Documents	206	1 <i>75</i>	85%	92%
Projects Certified by Right of Way	322	270	84%	92%
Projects Designed and Ready for Construction	340	293	86%	91%
Capital Value Ready for Allocation	\$4,204 M	\$3,256 M	77%	86%
Projects Constructed	261	159	61%	87%




Five-Year Trend; DED and PAED

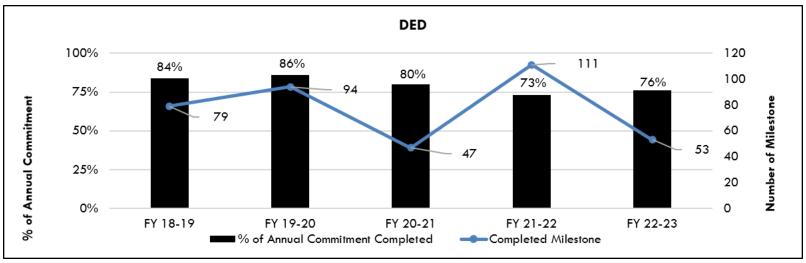


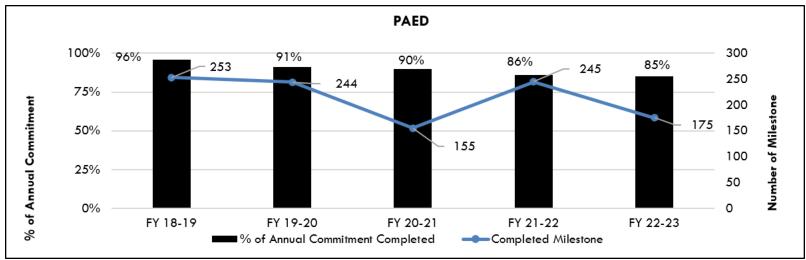




Five-Year Trend; RoW Cert and RTL

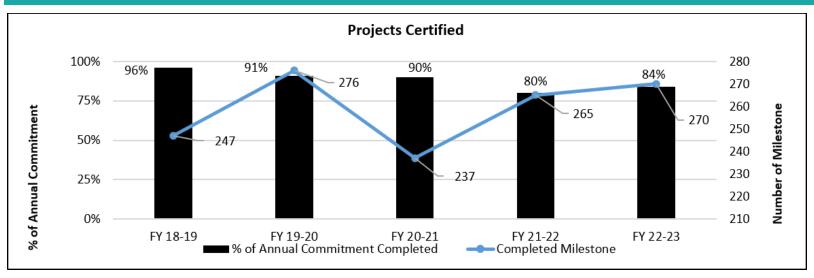


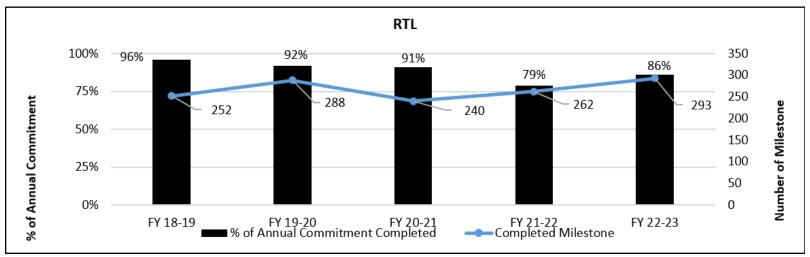



Five-Year Trend; Construction Value and CCA

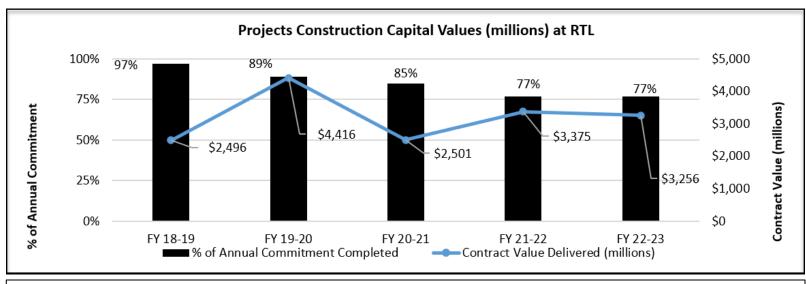





End of Construction-Completed STIP and SHOPP Projects

Project Construction Costs¹

Program	Completed Projects	Expended	Budget ²	Savings	Percent Expended	Last Five Fiscal Year Average
STIP	14	\$1,506 M	\$1,683 M	\$1 <i>77</i> M	90%	91%
SHOPP	255	\$3,340 M	\$3,872 M	\$532 M	86%	89%

¹ Construction costs are calculated 6 months after the end of construction.



² Budget is the sum of all approved Commission allocations or the approved programmed amounts if no allocation existed.


Current* Status – Capital Outlay Delivery

Measure	FY 2023-24 Planned	Completed	
Draft Environmental Documents	86	8	
Project Approval, Environmental Documents	199	1 <i>7</i>	
Projects Certified by Right of Way	282	28	
Projects Designed and Ready for Construction	287	11	
Capital Value Ready for Allocation	\$5,313 M	\$97 M	
Projects Constructed	274	38	

^{*}Data as of October 8, 2023




Current Bidding Environment - Bidders

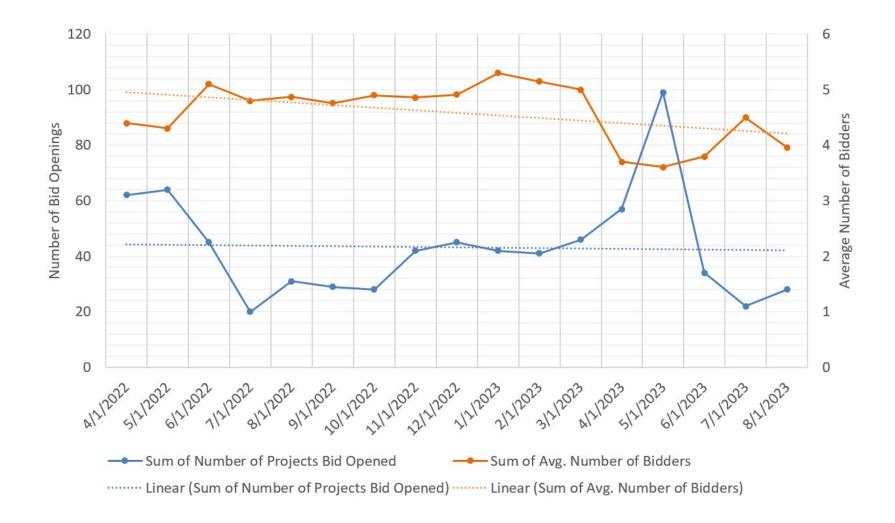



Current Bidding Environment - Estimates



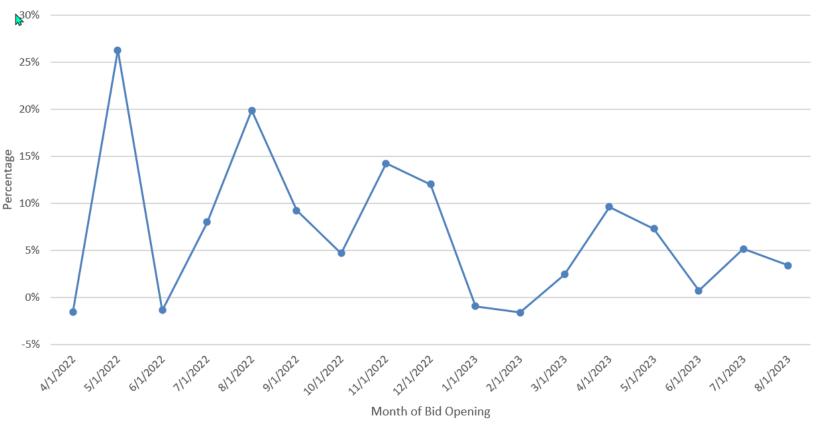





Current Bidding Environment - Material





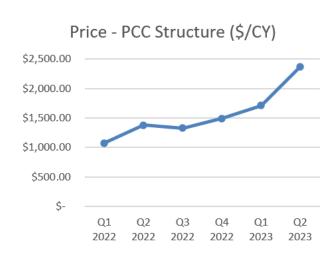









Thank You!

